

Planning Process Group

Input


- Project Charter
- Outputs from planning
- OPA
- EEF
- Project Charter
- Stakeholder register
- Project Charter
- Requirements Documentation
- OPA
- Project Scope Statement
- Requirements documentation
- OPA
- Scope baseline
- EEF
- OPA
- Activity List
- Activity Attributes
- Milestone list
- Project Scope Statement
- OPA
- Activity List
- Activity Attributes
- Resource Calendar
- EEF
- OPA
- Activity List
- Activity Attributes
- Activity Resource Requirements
- Resource Calendar
- Project Scope Statement
- EEF
- OPA
- Activity List
- Activity Attributes
- Project Schedule Network Diagram
- Activity Resource Requirements
- Resource Calendar
- Activity Duration Estimates
- Project Scope Statement
- EEF
- OPA

Output


- Mgmt plans KA
- PP
- Mgmt plans mst
- Project documents
- Project Performance Baseline
- Requirements documentation
- Requirements mgmt plan
- Requirements traceability matrix
- Project Scope Statement
- Updt. Project doc's
- WBS
- WBS Dictionary
- Scope baseline
- Updt. Project doc's
- Activity list
- Activity attributes
- Milestone list
- Project Schedule Network Diagram
- Updt. Project doc's
- Activity Resource Requirements
- RRS
- Updt. Project doc's
- Activity Duration Estimate
- Updt. Project doc's
- Project Schedules
- Schedule Baseline
- Schedule Data
- Updt. Project doc's

Processes


4.2 Develop project mgmt. plan

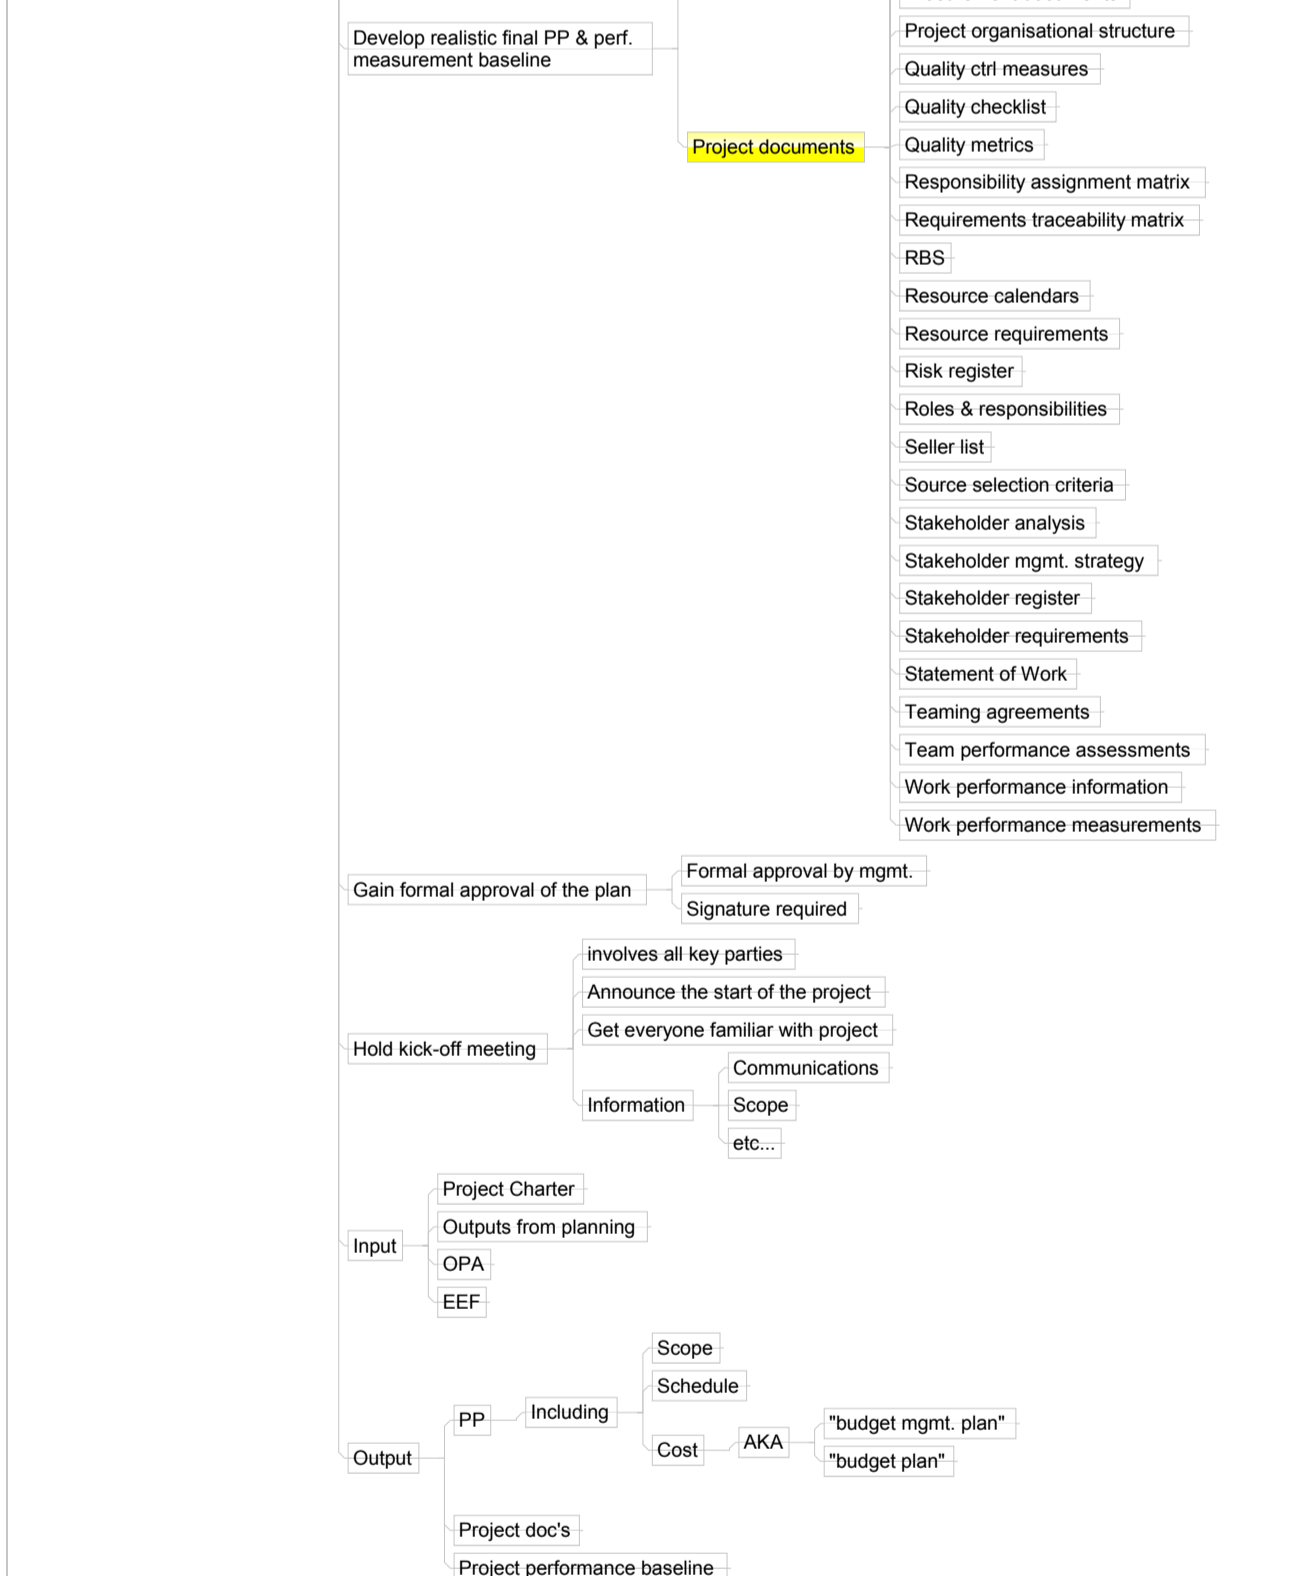

4.1 Collect requirements

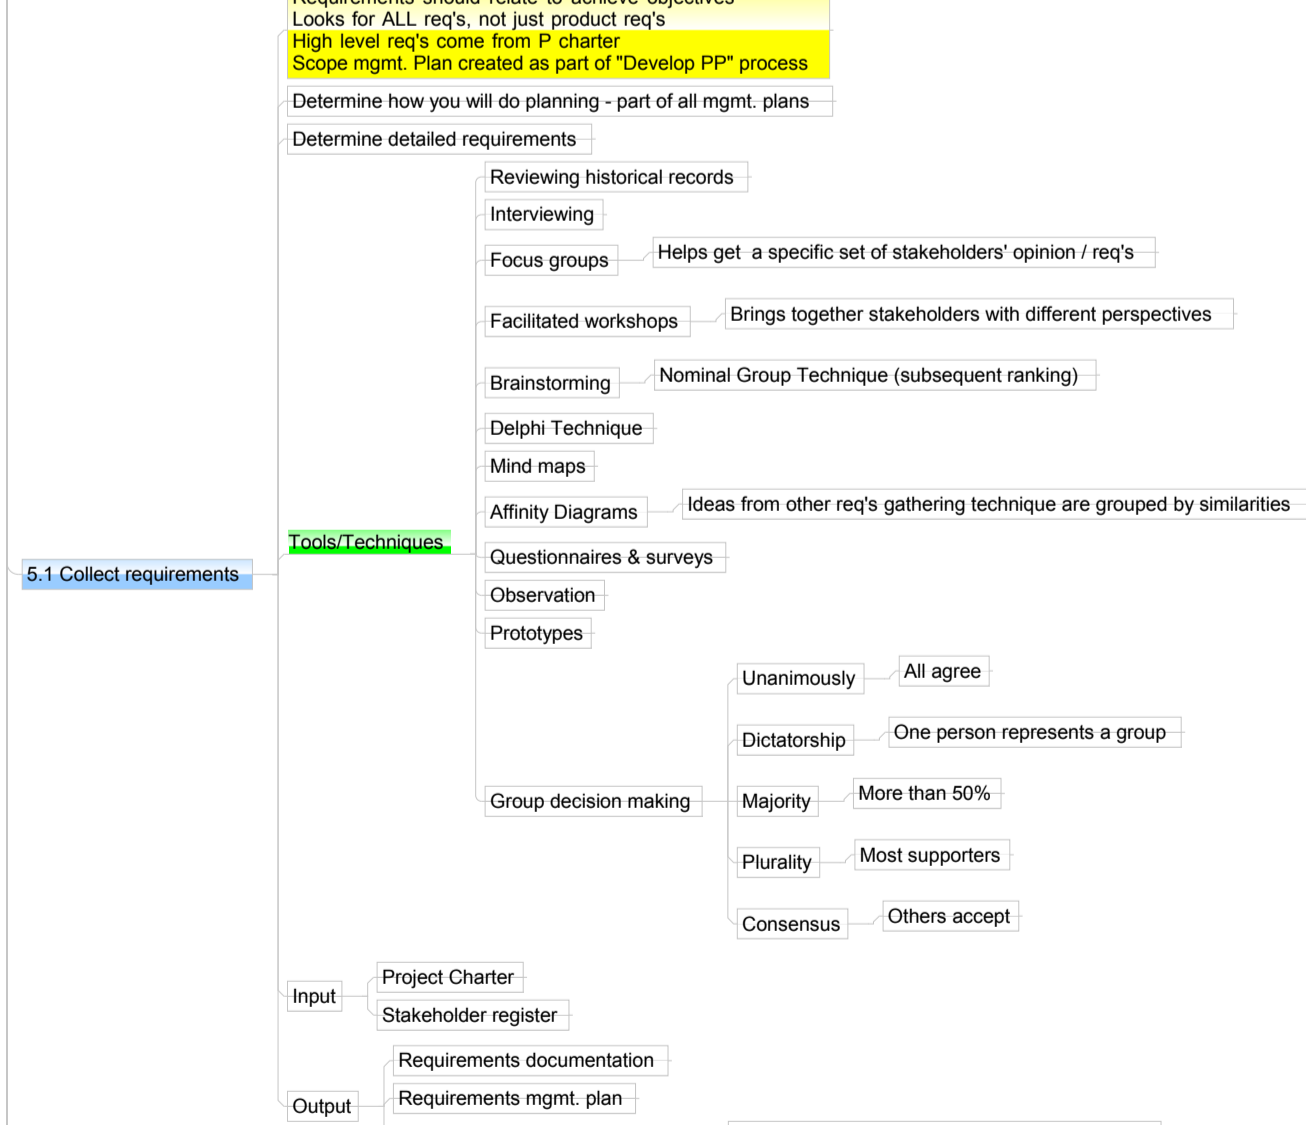

5.2 Define scope

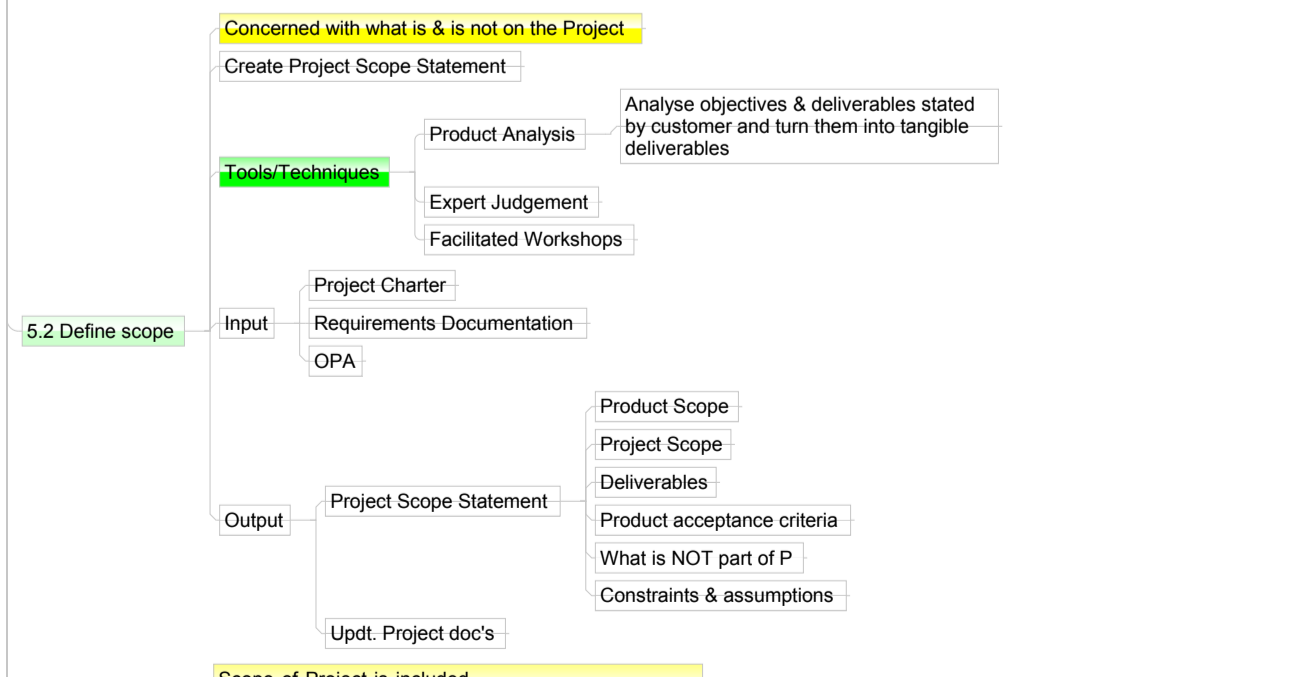

5.3 Create WBS

